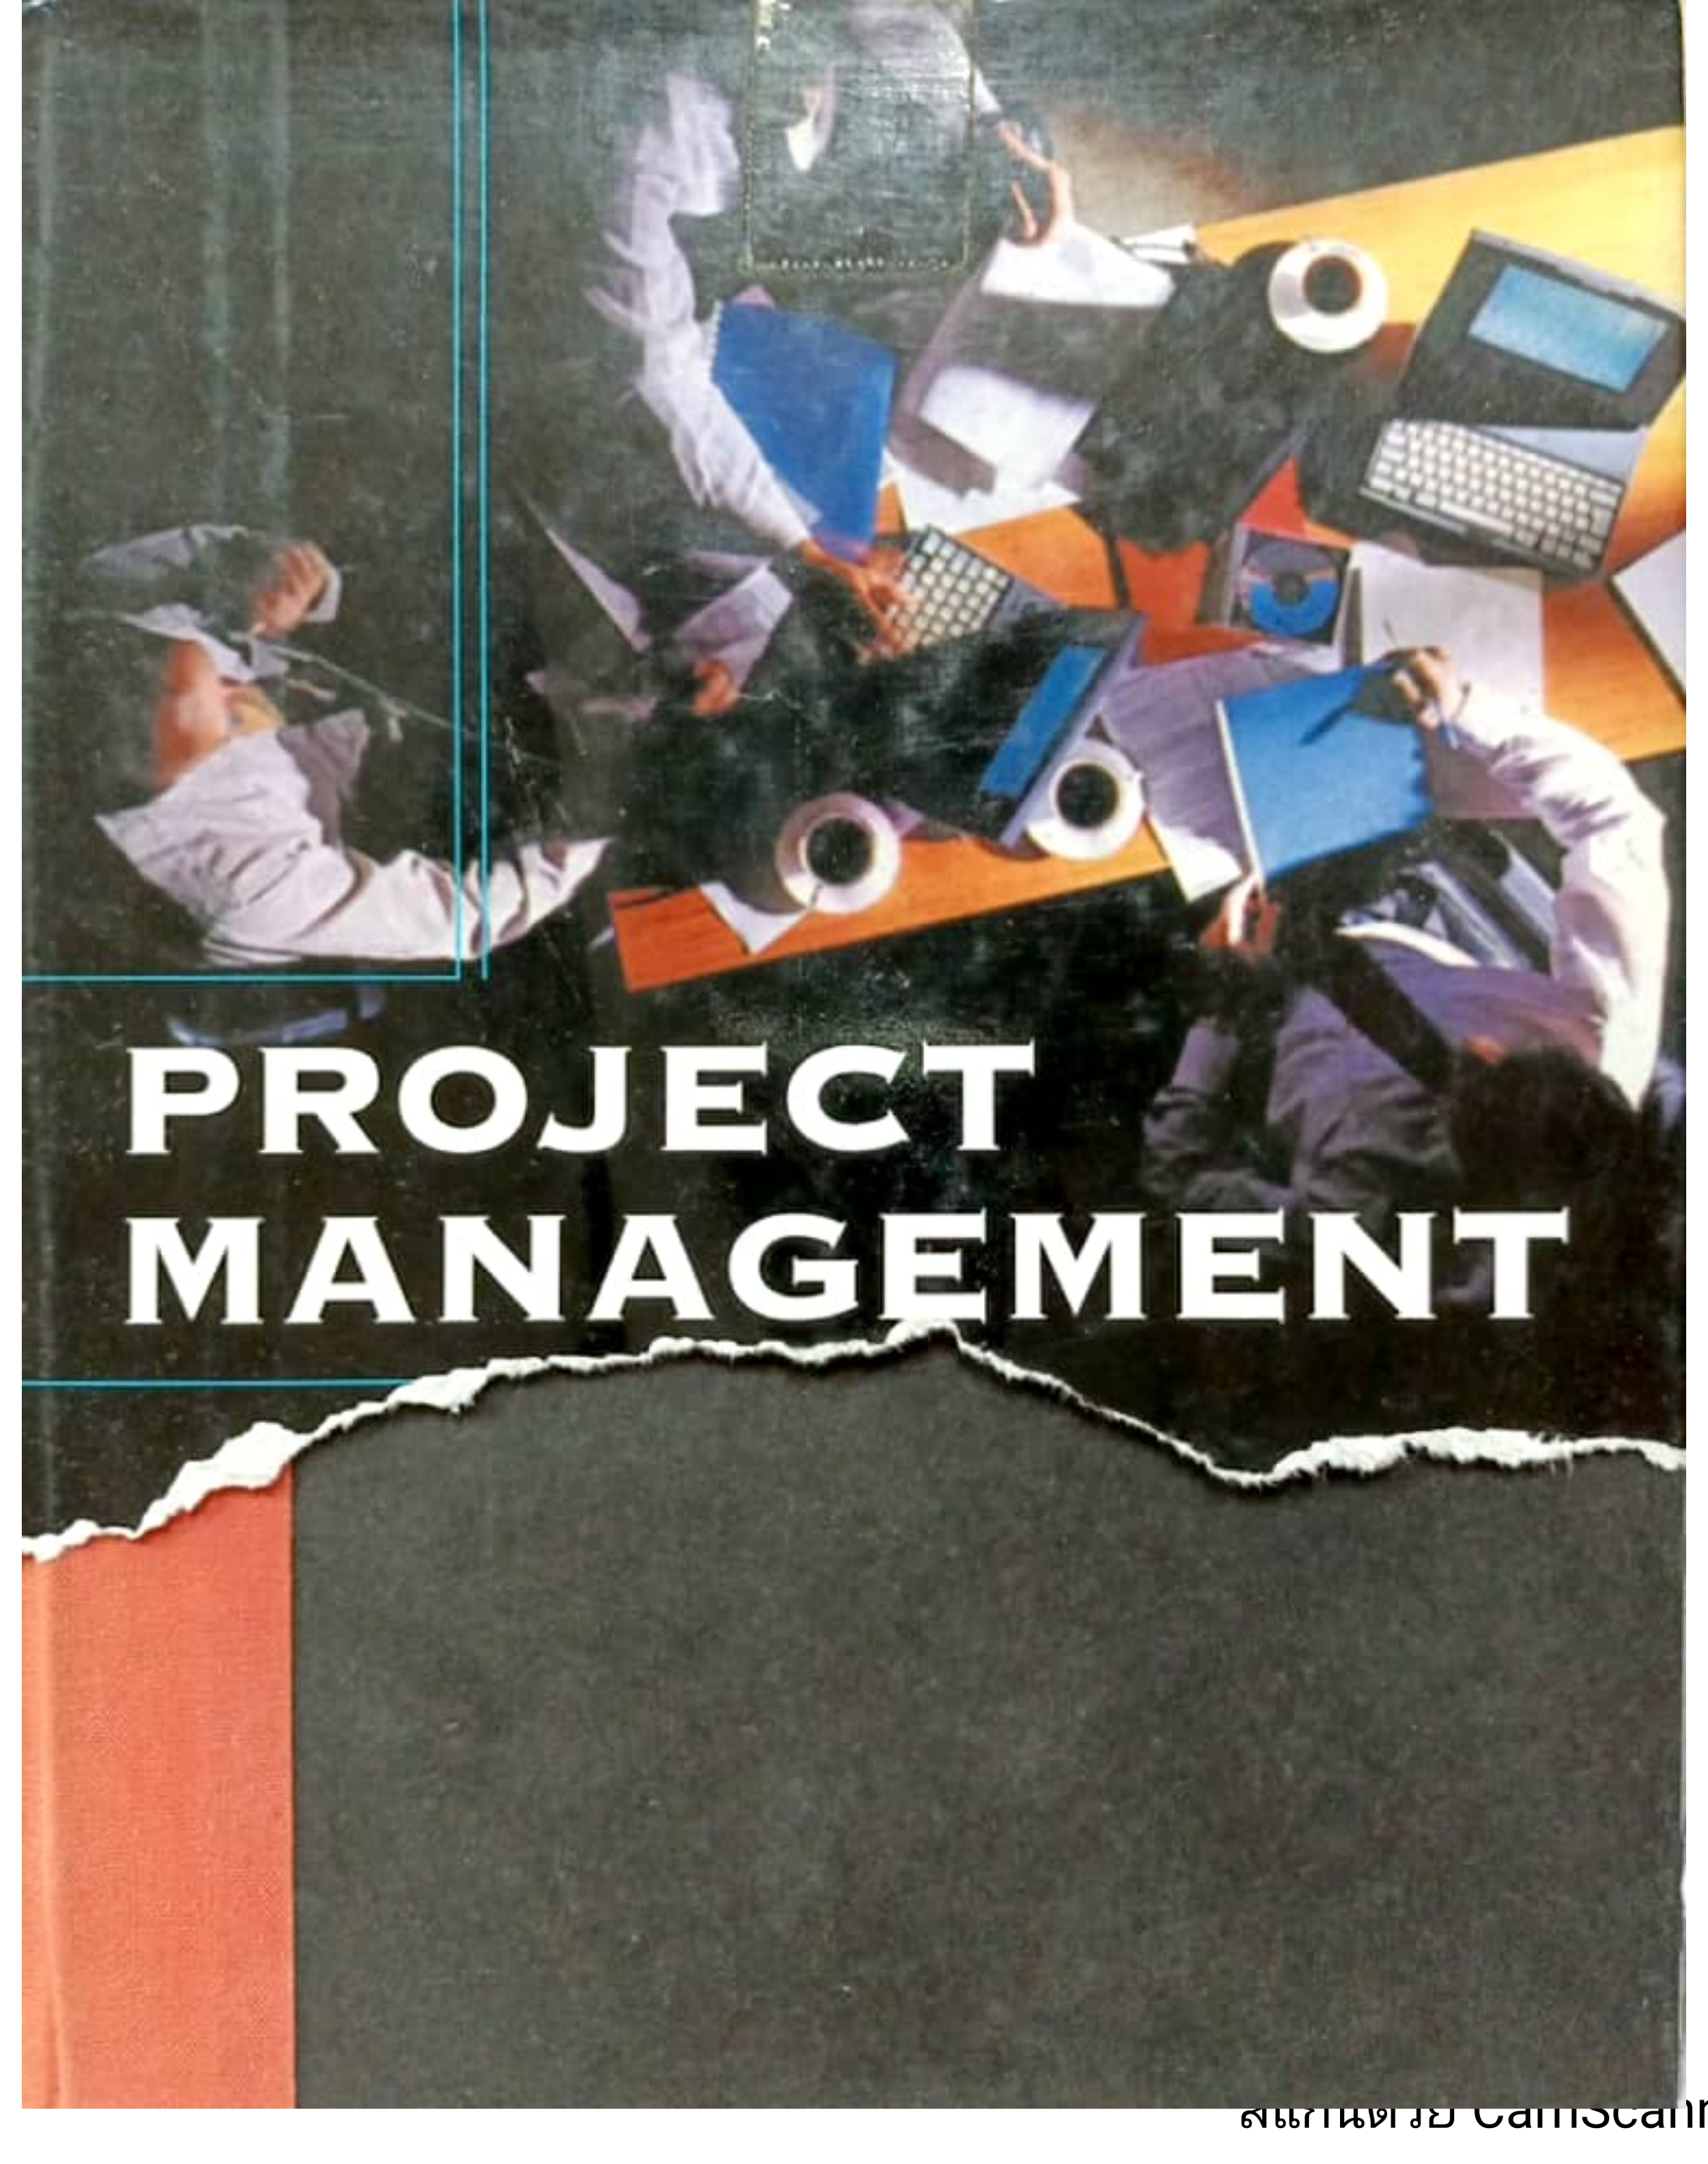


A collage of project management related items including a laptop, papers, and a CD-ROM. The items are arranged in a circular pattern on a dark background. The laptop is on the right, with a CD-ROM next to it. Papers and folders are scattered around. The text "PROJECT MANAGEMENT" is written in large, bold, white capital letters across the middle of the collage.

PROJECT MANAGEMENT

CONTENTS

PREFACE xi

1 Project Management Today 1

- Characteristics of Projects 1
- The Project Life Cycle 3
- Project Management in Action: A Project Management Sampler 4
- The Project Manager 7
- The Age of Project Management 8
- Project Management in Action: The Best Wireless Phone on the Market 9
- Project Management Today—An Integrative Approach 10
- Summary 15

2 Aligning of Projects with Organization Strategies 17

- Projects and the Strategic Plan 17
- The Strategic Management Process: An Overview 18
- Project Management in Action: Sample Strategies to Recapture Market Growth 21

- Absence of a Priority System Linked to Strategy Creates Problems 26
- Project Management in Action: The SAS Turnaround 28
- Moving to an Effective Project Selection System 30
- A Generic Project Portfolio Management System 34
- Project Management in Action: Y2K Projects 38
- Assessing the Effectiveness of the Priority System over the Long Haul—The Balanced Scorecard Model 44
- Summary 45

3 Organization: Structure and Culture 46

- Organizing Projects within the Functional Organization 47
- Organizing Projects as Dedicated Teams 49
- Organizing Projects within a Matrix Arrangement 51

Project Management in Action: Projectitis: The Dark Side of Project Teams	52	Macro versus Micro Estimating	99
Organizing Projects within Virtual Organizations	56	Estimating Project Times and Costs	101
Choosing the Right Project Management Structure	59	Project Management in Action: Estimate Accuracy During Project Life Cycle	106
Project Management in Action: The Project Management Office	60	Level of Detail	108
Organizational Culture	61	Developing Budgets	109
Identifying Cultural Characteristics	64	Estimating Guidelines for Times, Costs, and Resources	113
Implications of Organizational Culture for Organizing Projects	67	Refining Estimates and Contingency Funds	115
Project Management in Action: Matrix Problems at DEC	68	Project Management in Action: How Do You Estimate the Cost of a Nuclear Power Plant?	115
Summary	69	Creating a Database for Estimating	118
4 Defining the Project	71	Summary	119
Step 1: Defining the Project Scope	72	6 Developing a Network Plan	121
Project Management in Action: Operation Keiko Lift	75	The Project Network	121
Project Management in Action: Examples of Project Scope Statements	76	From Work Package to Network	122
Step 2: Establishing Project Priorities	79	Constructing a Project Network	125
Project Management in Action: Year 2000 Olympic Games—Sydney, Australia	81	Activity-On-Node (AON) Fundamentals	126
Step 3: Creating the Work Breakdown Structure	83	Project Management in Action: The Yellow Sticky Approach	129
Step 4: Integrating the WBS with the Organization	87	Start and Finish Network Computations	131
Step 5: Coding the WBS for the Information System	89	The Network Computation Process	132
Project Rollup	90	Project Management in Action: The Critical Path	138
Process Breakdown Structure	91	How the Information of the Forward and Backward Pass Is Used	138
Responsibility Matrices	93	Loose Ends	139
Summary	95	Extended Network Techniques from Practice	144
5 The Challenge of Estimating Project Times and Costs	96	Lags	145
Factors Influencing the Quality of Estimates	97	Project Management in Action: Concurrent Engineering	147
		An Example Using Lag Relationships	150
		Summary	151

7 Managing Risk 153

- Risk Management Process 153
- Step 1: Identifying Sources of Risk 156
- Step 2: Risk Analysis and Assessment 158
- Project Management in Action:
 - Semiquantitative Risk Approach 163
- Step 3: Responding to Risks 164
- Project Management in Action: From
 - Dome to Dust 166
- Contingency Planning 167
- Project Management in Action: Risk
 - Management at the Top of the World 171
- Establishing Contingency Reserves 174
- Step 4: Risk Control 176
- Summary 180

8 Resource Scheduling 181

- Scheduling Problems 181
- Types of Project Constraints 182
- Kinds of Resource Constraints 183
- Scheduling Resources for Utilization and
 - Given Availability 184
- Project Management in Action: Assessing
 - Resource Allocation 197
- Project Management in Action:
 - U.S. Forest Service Resource Shortage 198
- Splitting/Multitasking 198
- The Critical-Chain Approach 199
- Benefits of Scheduling Resources 205
- Assigning Project Work 205
- Project Management in Action: Assigning
 - Geeks to Projects 206
- Multiproject Resource Schedules 206
- Summary 208

9 Accelerating Project Completion 210

- The Challenge 210
- Rationale for Reducing Project Time 211
- Project Time Reduction Procedure 212

- Project Management in Action:
 - Responding to the Northridge Earthquake 213

- Project Management in Action:
 - I'll Bet You . . . 222

- Project Management in Action: The Fastest
 - House in the World 225

- Summary 228

10 Managing Project Stakeholders 230

- Managing versus Leading 230
- Managing Project Stakeholders 232
- Influence as Exchange 236
- Social Network Building 240
- Project Management in Action: Leading at
 - the Edge 247
- Ethics and Project Management 249
- Building Trust: The Key to Exercising
 - Influence 250
- Qualities of an Effective Project
 - Manager 252
- Project Management in Action: Profile of a
 - Prospective Project Coordinator 254
- Summary 256

11 Managing Project Teams 258

- The Five-Stage Team Development
 - Model 260
- Situational Factors Affecting Team
 - Development 261
- Building a High-Performing Project
 - Team 262
- Recruiting Project Members 263
- Project Management in Action: Managing
 - Martians 265
- Conducting Project Meetings 266
- Project Management in Action: Software
 - Development Teams at Microsoft 270
- Establishing a Team Identity 271
- Creating a Shared Vision 272
- Managing Project Reward Systems 275

- Project Management in Action: "Rat Track Fax" Galvanizes ELITE Team at Newspaper 276
 - Managing the Decision-Making Process 278
 - Managing Conflict within the Project Team 280
 - Team-Building Sessions 283
 - Managing Virtual Project Teams 285
 - Project Team Pitfalls 287
 - Overcoming Barriers to Performance 289
 - Project Management in Action: Managing Low-Priority Projects 291
 - Summary 292
- 12 Managing Projects across Organizations 293**
- The Genesis of Project Partnering 294
 - Project Management in Action: The Kodak Orion Project 297
 - Preproject Activities: Setting the Stage for Successful Partnering 298
 - Project Implementation: Sustaining Collaborative Relationships 301
 - Project Management in Action: Incentive System for a Partnering Project 302
 - Project Completion: Celebrating Success 304
 - Why Project Partnering Efforts Succeed or Fail 305
 - Project Management in Action: Competing against Giants 305
 - The Art of Negotiating 307
 - A Note on Managing Customer Relations 313
 - Summary 316
 - Appendix 12A: Contract Management 317
 - Project Management in Action: Can Partnering Work in the Public Sector? 319
- 13 Monitoring Project Performance 322**
- The Project Control Process 322
 - Monitoring Time Performance 325
 - An Integrated Cost/Schedule System 327
 - Project Management in Action: Status Reports at Microsoft 328
 - The Earned Value System 329
 - Developing a Status Report: A Hypothetical Example 336
 - Indexes 343
 - Forecasting Final Project Cost 346
 - Project Management in Action: Trojan Decommissioning Project 347
 - Other Control Issues 349
 - Project Management in Action: A Pseudo-Percent Complete Approach 349
 - Summary 353
- 14 Project Audit and Closure 354**
- Project Audits 355
 - The Project Audit Process 357
 - Project Management in Action: Operation Eagle Claw 360
 - The Audit Report 361
 - Project Management in Action: Lessons Learned: Bell Canada Business Transformation Project 363
 - Project Management in Action: Hewlett-Packard's Project Management Initiative 365
 - Project Closure 366
 - Team, Team Member, and Project Manager Evaluations 372
 - Summary 376
 - Project Management in Action: 360° Feedback 377
- 15 Project Management: The Future 379**
- Emergence of Project-Driven Organizations 380

Project Management in Action: The International Space Station (ISS) Project	381
Project Management in Action: The Human Genome Project	382
Project Management Maturity Model	383
Career Paths in Project Management	387
Project Management in Action: Harvesting Project Leaders	389
Project Management in Action: Works Well with Others	391
Summary	393
Conclusions	394
Notes	395
Glossary	409
Acronyms	415
Project Management Equations	416
Index	417
